



Executive Steering Committee (ESC) Update

Minnesota Eligibility Technology System (METS)

Deb Tibstra | Director – Application Services Division, MNIT Services @ DHS/MNsure –

October 24, 2017

- Winter Release Update
- Open Enrollment Readiness
- 2018 Roadmap Planning Update
- Roadmap & Project Overviews
- Detailed Project Status Update

- MMIS Interface (Includes Redesign)
- Notices (Includes Redesign)
- Carrier Integration
 - Automated 1095-A Corrections & Voids, 1095-A Enrollment Caps Phase 2, 834 EDI: Member Level Terms
- Periodic Data Match / FTI Masking
- Defects

Open Enrollment Readiness

- Performance & Load Testing - To ensure that system response times for critical transactions meet or exceed defined performance requirements.
- Call Center & Website – Implementing lessons learned and preparing for high-volume situations.
- MNIT Staffing & Coverage – Coordinating staffing and rapid-response teams to address unexpected issues should they arise.

2018 Roadmap Planning

1. Identify and score new proposed project work
2. Determine capacity, define project scope and gather Level of Effort (LOE) for proposed 2018 projects and ongoing efforts
3. Rank and prioritize projects (Blueline)
4. Identify Release timeframe
5. PMT Recommendation
6. ESC Approval

METS 2017 Release Roadmap

| |
|--------------------------------|
| Work Incomplete |
| Work Completed |
| Work Currently Underway |
| XL = "Mega Project" |


| Spring 2017 | Summer 2017 | Fall 2017 | Winter 2017 |
|--|---|------------------------------------|--|
| Assister Portal | Cúram Eligibility System Upgrade XL | MMIS Interface (Includes Redesign) | MMIS Interface (Includes Redesign) |
| Notices (Includes Redesign) | Supervisor Workspace / Org Location Structure | Notices (Includes Redesign) | Notices (Includes Redesign) |
| PRISM Defects | Notices (Includes Redesign) | Carrier Integration | Carrier Integration |
| Cost Sharing | MMIS Interface (Includes Redesign) | Trigger of FTR via Federal Hub | Periodic Data Match (PDM) /FTI Masking |
| Federal Poverty Level (FPL) - MA Annual Update | Defects | Defects | Defects |
| MMIS Interface (Includes Redesign) | | | |
| Defects | | | |

Ongoing Efforts


| |
|--------------------------------------|
| 1095-A Operations |
| 1095-B Operations |
| Data Access and Management - Reports |
| Infrastructure Improvements |
| MAXIS to METS Migration |
| Premium Reconciliation |
| Periodic/Annual Work |
| Renewals Operations |

2017 Carrier Integration Project Roadmap

| |
|-------------------------|
| Work Incomplete |
| Work Completed |
| Work Currently Underway |
| Work On Hold |

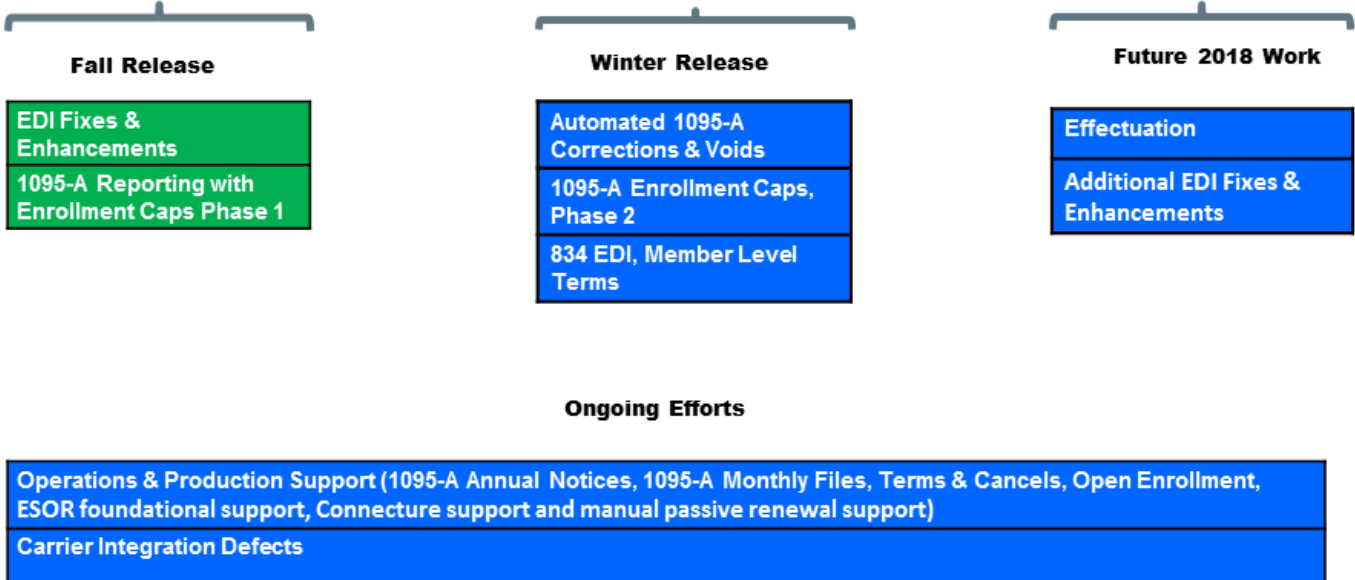

IT Release Plan: Public Program Work— Ongoing Efforts

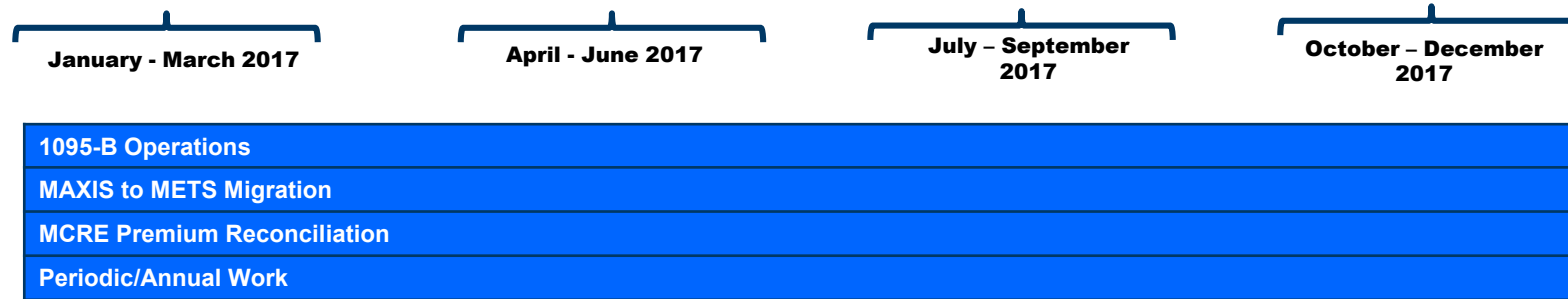

Program Status

As of 10/20/17

| Project Name | Release | Scope | Schedule | Issues | Risk | Overall |
|---|------------------|-------|----------|--------|--------|---------|
| Periodic Data Match / FTI Masking | 17.4 Winter 2017 | Green | Green | Green | Green | Green |
| Defects 17.4 | 17.4 Winter 2017 | Green | Green | Green | Green | Green |
| Notices 17.4 | 17.4 Winter 2017 | Green | Green | Green | Green | Green |
| Reasonable Opportunity Period (ROP) - Phase 1 | 18.1 Spring 2018 | Green | Green | Green | Yellow | Yellow |
| DEED for Verification of Income | 18.1 Spring 2018 | Green | Green | Green | Yellow | Yellow |
| Cúram Instance Alignment | 18.2 Summer 2018 | Green | Yellow | Green | Green | Yellow |
| 1095-A Operations | Ongoing | Green | Green | Green | Green | Green |
| 1095-B Operations | Ongoing | Green | Green | Green | Green | Green |
| Carrier Integration | Ongoing | Green | Green | Green | Green | Green |
| Data Access & Management (Reports) | Ongoing | Green | Green | Yellow | Green | Yellow |
| Infrastructure Improvements | Ongoing | Green | Green | Green | Green | Green |
| MAXIS to METS Migration | Ongoing | Green | Green | Green | Green | Green |
| MCRE Premium Reconciliation | Ongoing | Green | Green | Green | Green | Green |
| MMIS Interface (Includes Redesign) | Ongoing | Green | Red | Red | Green | Red |
| Periodic / Annual Work | Ongoing | Green | Green | Green | Green | Green |
